



This presentation does not contain any proprietary, confidential, or otherwise restricted information

Conducting a 3D Converted Shear Wave Project to reduce exploration risk at Wister, CA

May 18, 2010

Skip Matlick
Ormat Nevada Inc.

Innovative Technologies

- Timeline
 - Project start October 2009
 - Project end date Q2 2011
 - Percent complete ~5%
- Budget
 - Total project funding \$8,525,515
 - DOE share \$4,475,015,
 - Ormat share \$4,050,500
 - Funding for FY10 ~\$8,400,000
- Barriers
 - Permit:
 - In case necessary, acquiring BLM drilling permits might effect the proposed timetable**
- Partners
 - ExplorTech LLC

The primary objective of this project is to conduct a 3C 3D (converted shear wave) seismic survey to reduce exploration risk by characterizing fault and fracture geometrics at Wister, CA.

The intent of the proposed program is to use a 3D seismic survey with converted shear waves combined with other available data to site and drill production wells at Wister, a blind geothermal resource.


This presentation does not contain any proprietary, confidential, or otherwise restricted information

- Principal Investigator
 - Skip Matlick (Ormat Nevada, Inc.)
- Co-investigator
 - John Arestad (ExplorTech LLC)
- DOE
 - GTP - DOE Golden Office

- Grant Awarded October 2009
- Design Survey January 2010 (Complete)
- Sign acquisition and processing 3C 3D seismic survey contracts (Complete)
- Forward Modeling (Complete)
- BLM Permits (In process)
- Phase I: Seismic Survey scheduled to start on Q2, 2010
- Phase II & III: Well Drilling and Testing scheduled to start on Q4, 2010
- Project completed Q2, 2011

Wister Location Map

WISTER LOCATION MAP
IMPERIAL VALLEY, CA

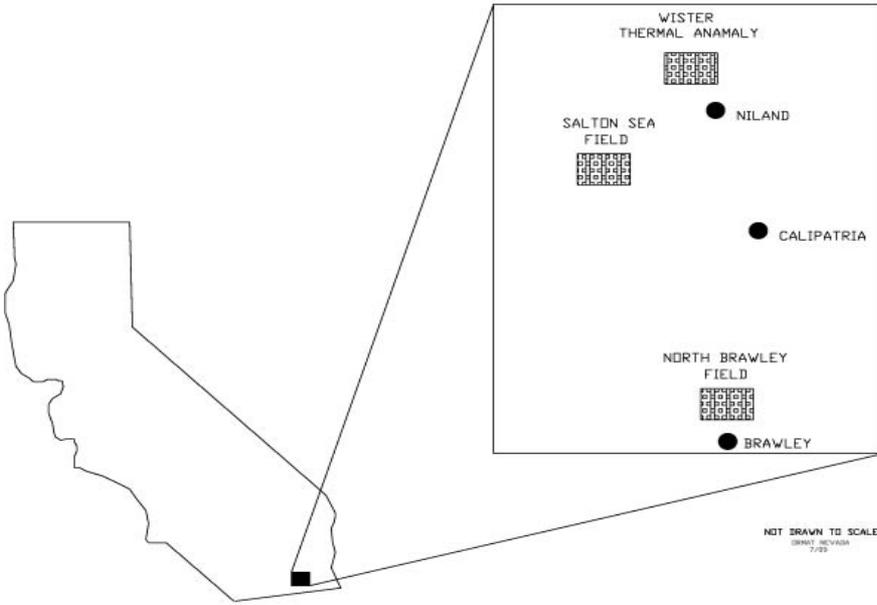

- Farming activity has destroyed surface geological features.
- Approximately 30 temperature gradient holes defined a 8°F/100 ft anomaly covering 2.5 square miles.
- In 1988, UNOCAL drill Well 88-1 to 3942 ft where the well bore collapsed after intersecting a large fracture.
- Attempts to salvage the well failed and UNOCAL converted the well to a Temperature Observation hole.
- Temperature measurements show that 88-1 has a conductive gradient to 3926 ft where is 342°F is measured.


- Over 1000 gravity measurements collected on a 250 m grid where used to calculate complete Bougeur anomaly values.
- Zonge Geosciences, Inc. modeled these data with regional gravity and magnetic data to product complete Bougeur, horizontal gravity gradient, and reduced to pole magnetic maps.

- **Phase I –Converted Wave Seismic Project**
 - Prepare forward models to determine probable seismic response.
 - Select contractors to acquire and process seismic data.
 - Obtain required permits.
 - Acquire 13.5 square miles of 3D seismic data using vibratory sources and multicomponent (3C) receivers.
 - Interactive processing of three data sets of 3C 3D three components.
 - Compressional (P-P) wave data
 - Fast (P-S1) converted shear-wave data
 - Slow (P-S2) converted shear-wave data
 - Interpretation of the 3C 3D seismic data.
 - Structural, amplitude, velocity-ratio, and anisotropy analysis
 - Integration with geological and other geophysical data
 - Prepare and present final report

- **Phase II & III– Drilling & Flow Testing**
 - Obtain permits.
 - Drill 2 production wells each ~6500 feet deep
 - Flow test each well
 - Using Ormat’s standard testing strategy
 - Record TPS surveys with pressure build up.
 - Reservoir properties (permeability, temperature, productivity, chemistry)

Project Total Budget: \$8,525,515
 \$4,475,015 DOE funding with 47.5% Ormat cost share

	Phase I	Phase II	Phase III	Total
Ormat Cost share	\$141,505	\$3,783,500	\$125,495	\$4,050,500
DOE Cost share	\$566,020	\$3,783,500	\$125,495	\$4,475,015
Cost Share %	20.0%	50.0%	50.0%	47.5%
	\$707,525	\$7,567,000	\$250,990	\$8,525,515

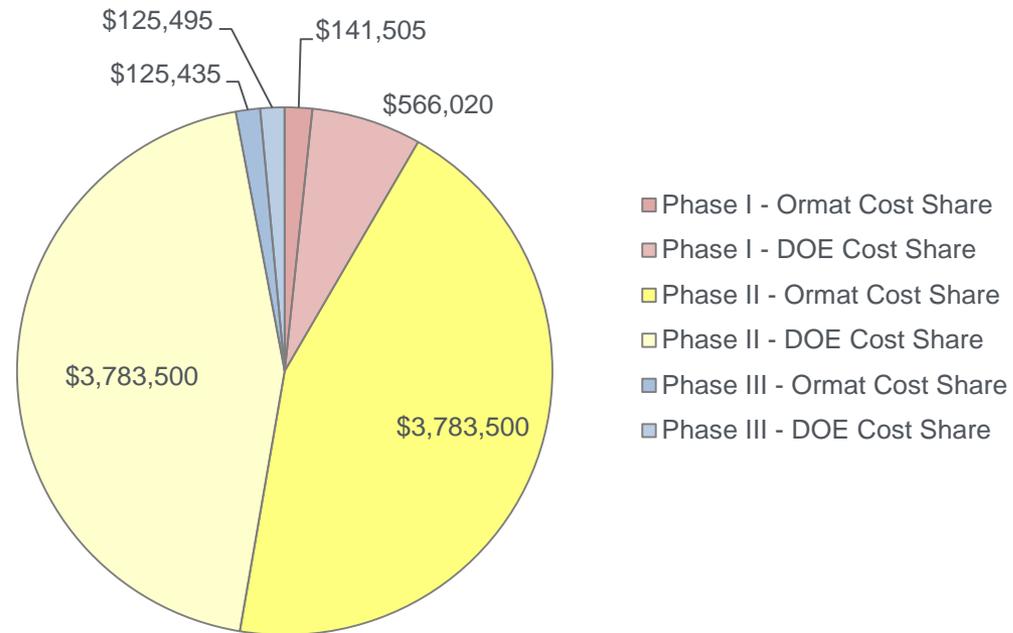

- Designed 3C 3D seismic survey.
- Signed contract with Dawson for acquisition.
- Signed contract with Fairfield for processing
- Generated forward models.
- Obtained land owners permission for data collection.
- Submitted permits applications to BLM.
 - Expect permit approval around end of May.

Land Owners Permission Map


Wister 3D
Client: Ormat Technologies

Goephones only
 BLM
 Permitted
 Contacted or Mailed
 No Permit


5-2-2010

N

T10S-R14E

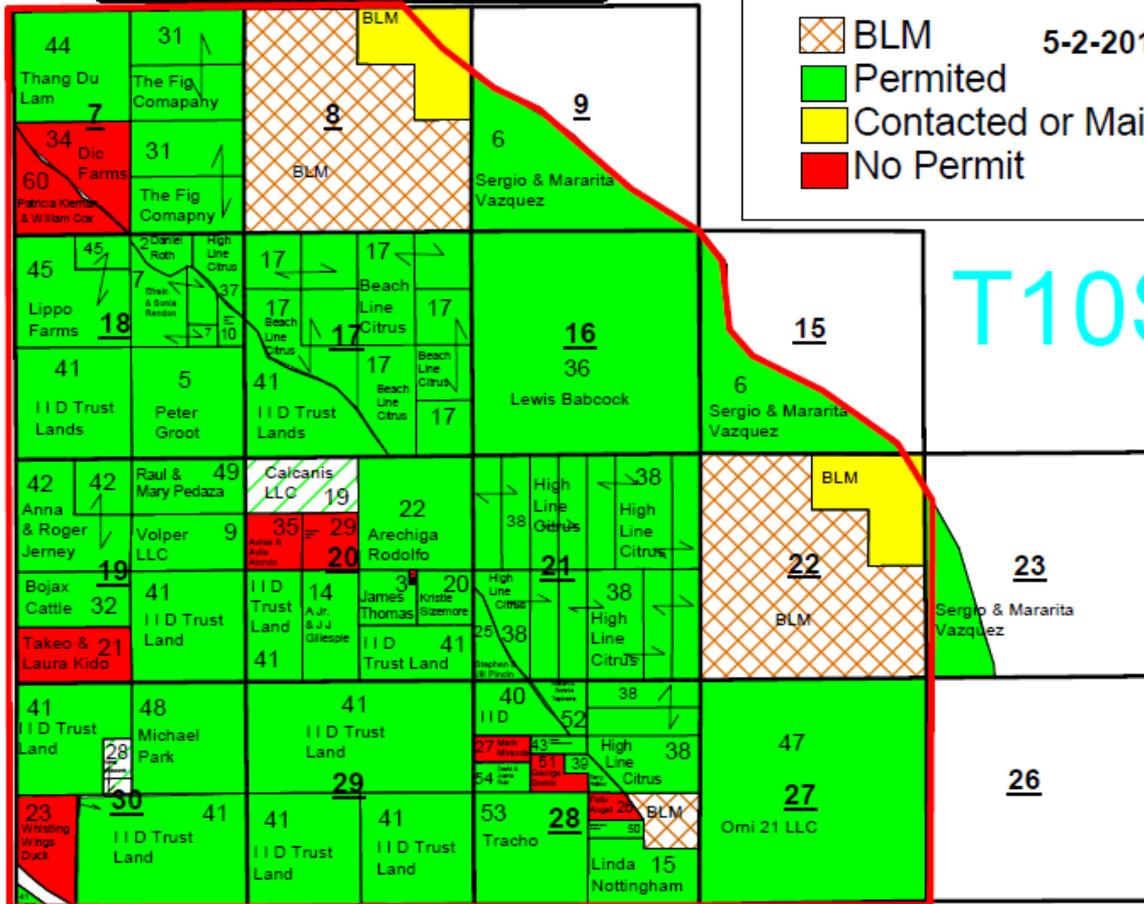

Survey Layout

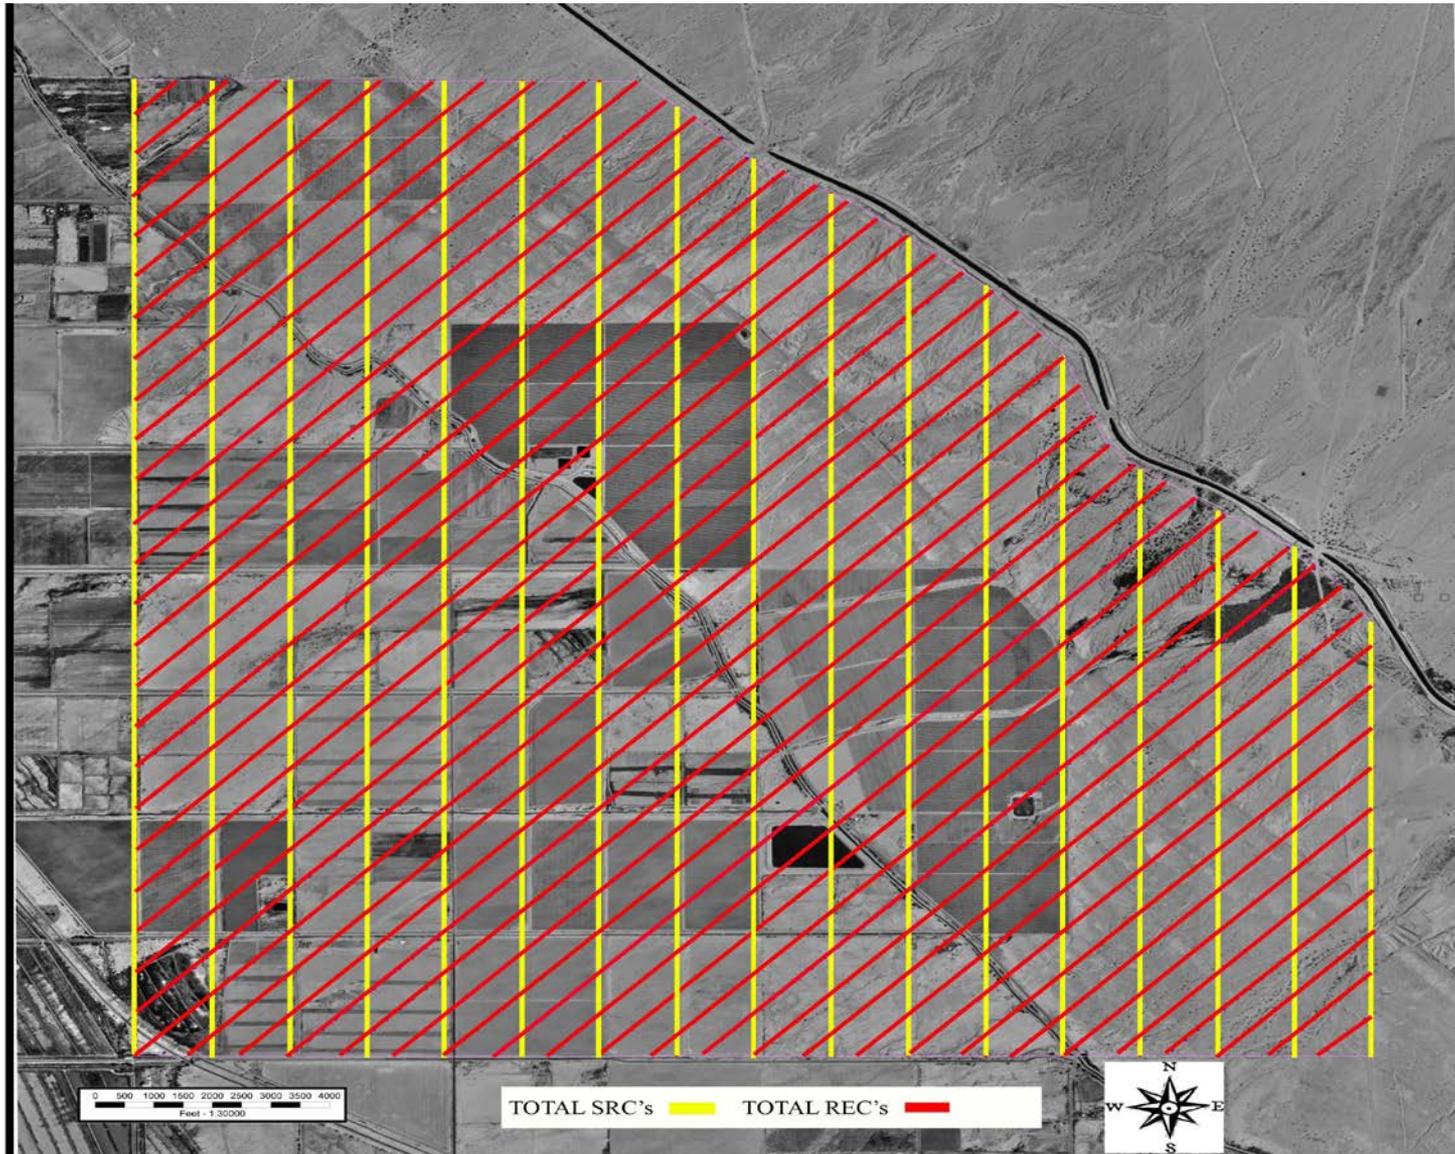

- DOE Grant Awarded October 2009.
- Seismic Acquisition & Processing Contracts signed.
- Survey Designed.
- Permits submitted to BLM Q2, 2010.
 - Expected BLM approval end of May, 2010
- Forward models generated.
- Seismic acquisition scheduled to start end of May 2010.
- Drilling estimated to spud on Q4 2010.
- Project completed Q2 2011.
